

PI
9-10-19

19-1001

TO BOARD OF PUBLIC WORKS City Engineer's Estimates

For WS-19-6 2019 SEAL COATING PROGRAM
TYPE OF WORK PERFORMED

CONSENT

August 21, 2019
DATE

1 & FINAL
NO.

SCOTT CONSTRUCTION, INC
CONTRACTOR

April 9, 2019
DATE OF CONTRACT

August 30, 2019
COMPLETION DATE

\$163,289.48
AMOUNT OF CONTRACT

Various

STREET

FROM - TO


CO#1 (\$23,990.49)
CO#2& \$1,006.31
TOTAL \$140,305.30

DESCRIPTION	NO. 1 PREVIOUSLY COMPLETED	NO. 2 COST WORK PREVIOUSLY COMPLETED	NO. 3 COMPLETED TO DATE	NO. 4 COST WORK COMPLETED TO DATE	NO. 5 DIFFERENCE COLUMNS 1 & 3	NO. 6 DIFFERENCE COLUMNS 2 & 4
SEE COMPUTER PRINTOUT						
INVOICE #: 4510						
INVOICE DATE: 8/14/19			FOR DETAILS			
TOTALS		\$0.00		\$140,305.30		\$140,305.30
PAYMENTS		\$0.00		\$140,305.30		\$140,305.30
AMOUNT DUE, FINAL PAYMENT						\$140,305.30

8-21-19
Date filed with Secretary
8-21-19
Date approved by Board

AMOUNT RECOMMENDED
\$140,305.30

BOARD
SIGNATURES

Mike Williams


Date Paid
Check No.
Voucher No.
Chg. 1100-32220-523110
Copy For
Council Board Voucher


Signature
8-21-19
CITY ENGINEER

PAY ESTIMATE WORKSHEET
 2019 SEAL COATING PROGRAM

PAY ESTIMATE NO. 1 & FINAL

DATE: August 21, 2019

CITY OF MANITOWOC CONTRACT NO. WS-19-6

Contractor: Scott Construction, Inc.

Contract Amount: \$163,289.48
 Change Order #1: (\$23,990.49)
 Change Order #2 - Final: \$1,006.31
\$140,305.30

CONTRACT DATE: April 9, 2019
 COMPLETION DATE: August 30, 2019

ITEM NO.	ITEM DESCRIPTION	UNIT	BID QUANTITIES	UNIT PRICE	QUANTITY PREVIOUS COMPLETED	COST WORK PREVIOUS COMPLETED	QUANTITY COMPLETED TO DATE	COST WORK COMPLETED TO DATE	% OF WORK COMPLETED TO DATE	QUANTITY DIFFERENCE	COST WORK DIFFERENCE
Seal Coating Various City Streets											
1	Mobilization	LS	1	\$10,000.00	0	\$0.00	1 *	\$10,000.00	100%	1.0	\$10,000.00
2	Traffic Control	LS	1	\$9,500.00	0	\$0.00	1 *	\$9,500.00	100%	1.0	\$9,500.00
3	Furnish & Install Base Sealcoating	SY	20,292	\$2.02	0	\$0.00	20,265.0 *	\$40,935.30	100%	20,265.0	\$40,935.30
4	Furnish & Install Surface Sealcoating	SY	32,167	\$2.45	0	\$0.00	32,600.0 *	\$79,870.00	101%	32,600.0	\$79,870.00
TOTAL FOR CONTRACT WS-19-6						\$0.00		\$140,305.30			\$140,305.30
PAYMENTS						\$0.00	100.00%	\$140,305.30		100.00%	\$140,305.30

NOTE: ASTERISK (*) DENOTES FINAL QUANTITY OR MEASUREMENT.

O.K. to Pay
 G.J.M.
 8/16/19

FINAL PAYMENT LIEN WAIVER

KNOW ALL MEN BY THESE PRESENTS that

WHEREAS, the undersigned Scott Construction, Inc

as General Contractor, entered into a Contract with the City of Manitowoc for the complete construction of City of Manitowoc, 2019 Seal Coating Program
Project NO. WS-19-6, and

WHEREAS, the undersigned has completed 100% of construction under the terms of the construction agreement,

NOW THEREFORE in consideration of final payment by the City of Manitowoc to the undersigned Scott Construction, Inc the undersigned hereby waives and releases any and all liens, claims or rights to file any lien or liens to the extent of the payment above referred to against the City of Manitowoc, and

The undersigned further states that all wages, materials, social security taxes, withholding taxes, sales and use taxes, permits, sub-contractors and materialmen have been fully paid and discharged for all work performed; workmen's compensation and other insurance premiums and all taxes have been fully paid and discharged.

The undersigned further agrees to save harmless the City of Manitowoc from any matter or thing arising from the filing of claims or liens by any workman, sub-contractor or materialmen in connection with the work performed.

IN WITNESS WHEREOF, the General Contractor by its' authorized representative has caused this waiver to be signed.

This 7th day of August, 2019.

Witness: Cathy M. Howell

John A. Scott
Contractor
John A. Scott, Vice President

SCOTT

CONSTRUCTION, INC.

ASPHALT SURFACING SINCE 1926

Box 340 LAKE DELTON, WI 53940 PH. 608.254.2555 FAX: 608.254.2249

Complete Asphalt Maintenance and Construction

WWW.SCOTTCONSTRUCT.COM



Invoice 4510

Bill to: City Of Manitowoc Manitowoc County 900 Quay Street Manitowoc, WI 54220	Job: S036H513 CITY OF MANITOWOC
---	------------------------------------

Invoice #: 4510	Date: 08/14/19	Customer P.O. #:
Payment Terms: 30 DAYS		Salesperson: MIKE BURNSIDE
Customer Code: 61059		

Remarks:


Description	Quantity	U/M	Unit Price	Extension
07/30/19 - 07/31/19				
SEAL COAT SURFACING AS PER CONTRACT:				
2019 SEAL COATING PROGRAM, WS-19-6				
MOBILIZATION	1.000	LS	10,000.00	10,000.00
TRAFFIC CONTROL	1.000	LS	9,500.00	9,500.00
FURNISH AND INSTALL BASE SEALCOATING	20,265.000	SY	2.02	40,935.30
FURNISH AND INSTALL SURFACE SEALCOATING	32,600.000	SY	2.45	79,870.00
			Subtotal:	140,305.30
			Total:	140,305.30

The first part of the document discusses the importance of maintaining accurate records of all transactions. It emphasizes that every entry should be supported by a valid receipt or invoice. This ensures transparency and allows for easy verification of the data.

In the second section, the author details the various methods used to collect and analyze the data. This includes both manual and automated processes. The goal is to ensure that the information is both reliable and up-to-date.

The third part of the report focuses on the results of the analysis. It shows a clear trend of growth over the period studied. This is attributed to several key factors, including improved operational efficiency and increased market demand.

Finally, the document concludes with a series of recommendations for future actions. These are designed to further optimize the current processes and address any identified weaknesses. The author believes that these steps will lead to continued success and stability.

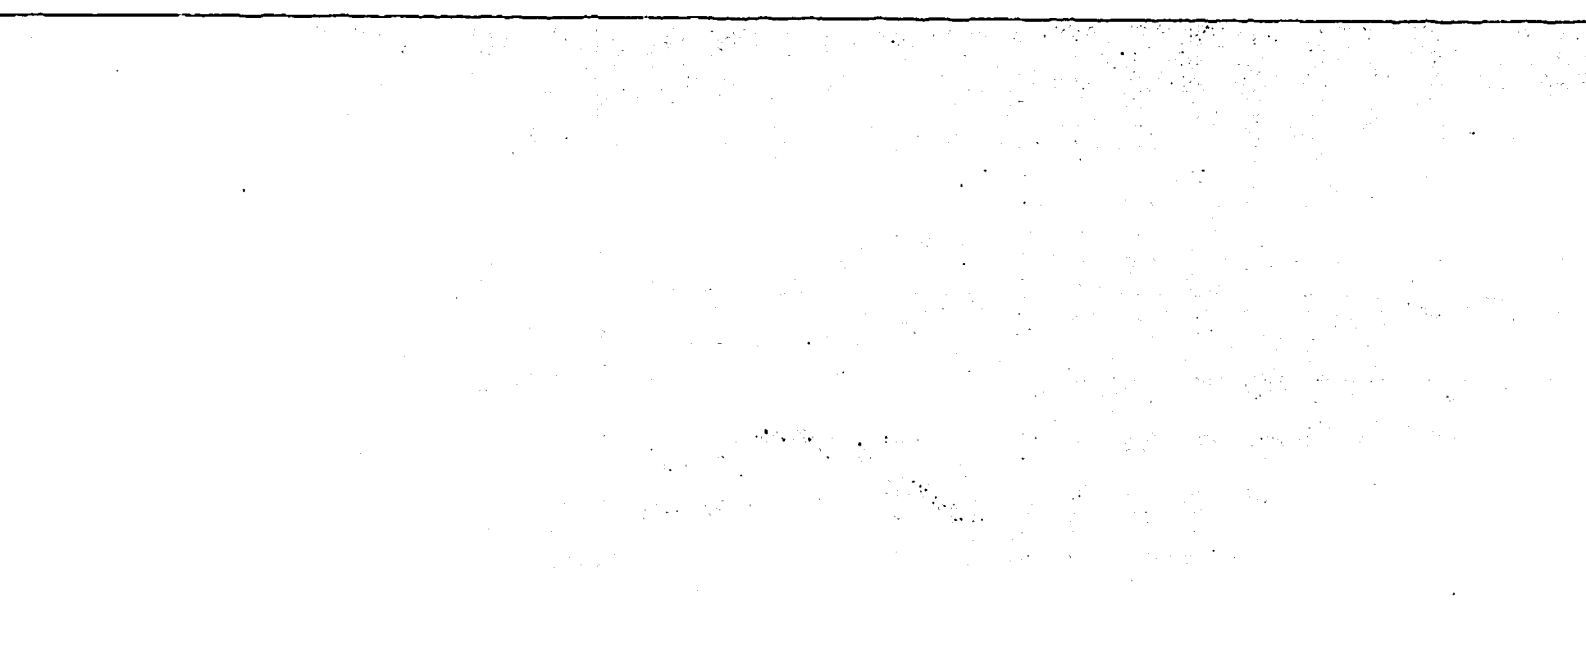

SINGLE SEAL

S. 31ST = 1712 SY
S. 30TH = 1992 SY
S. 32ND = 3240 SY
S. 34TH = 1463 SY
COOLIDGE PL = 1724 SY
COOLIDGE = 2204 SY

12,335

+ 20,265

TOTAL = 32,600 SY

SURFACE

DOUBLE SEAL

S. 8TH ST 1113
FLAMBEAU 3013
4702
2872
DEWEY 1488
Summit 3613
S. 11TH 3464

TOTAL = 29,265 SY

BASE
